
STAR GARDENS

KEDAKAL | PLOTS & STRAIGHT ROADS

Revision 04 | 46 farmhouse plots | Proposed 20 ft CC road network

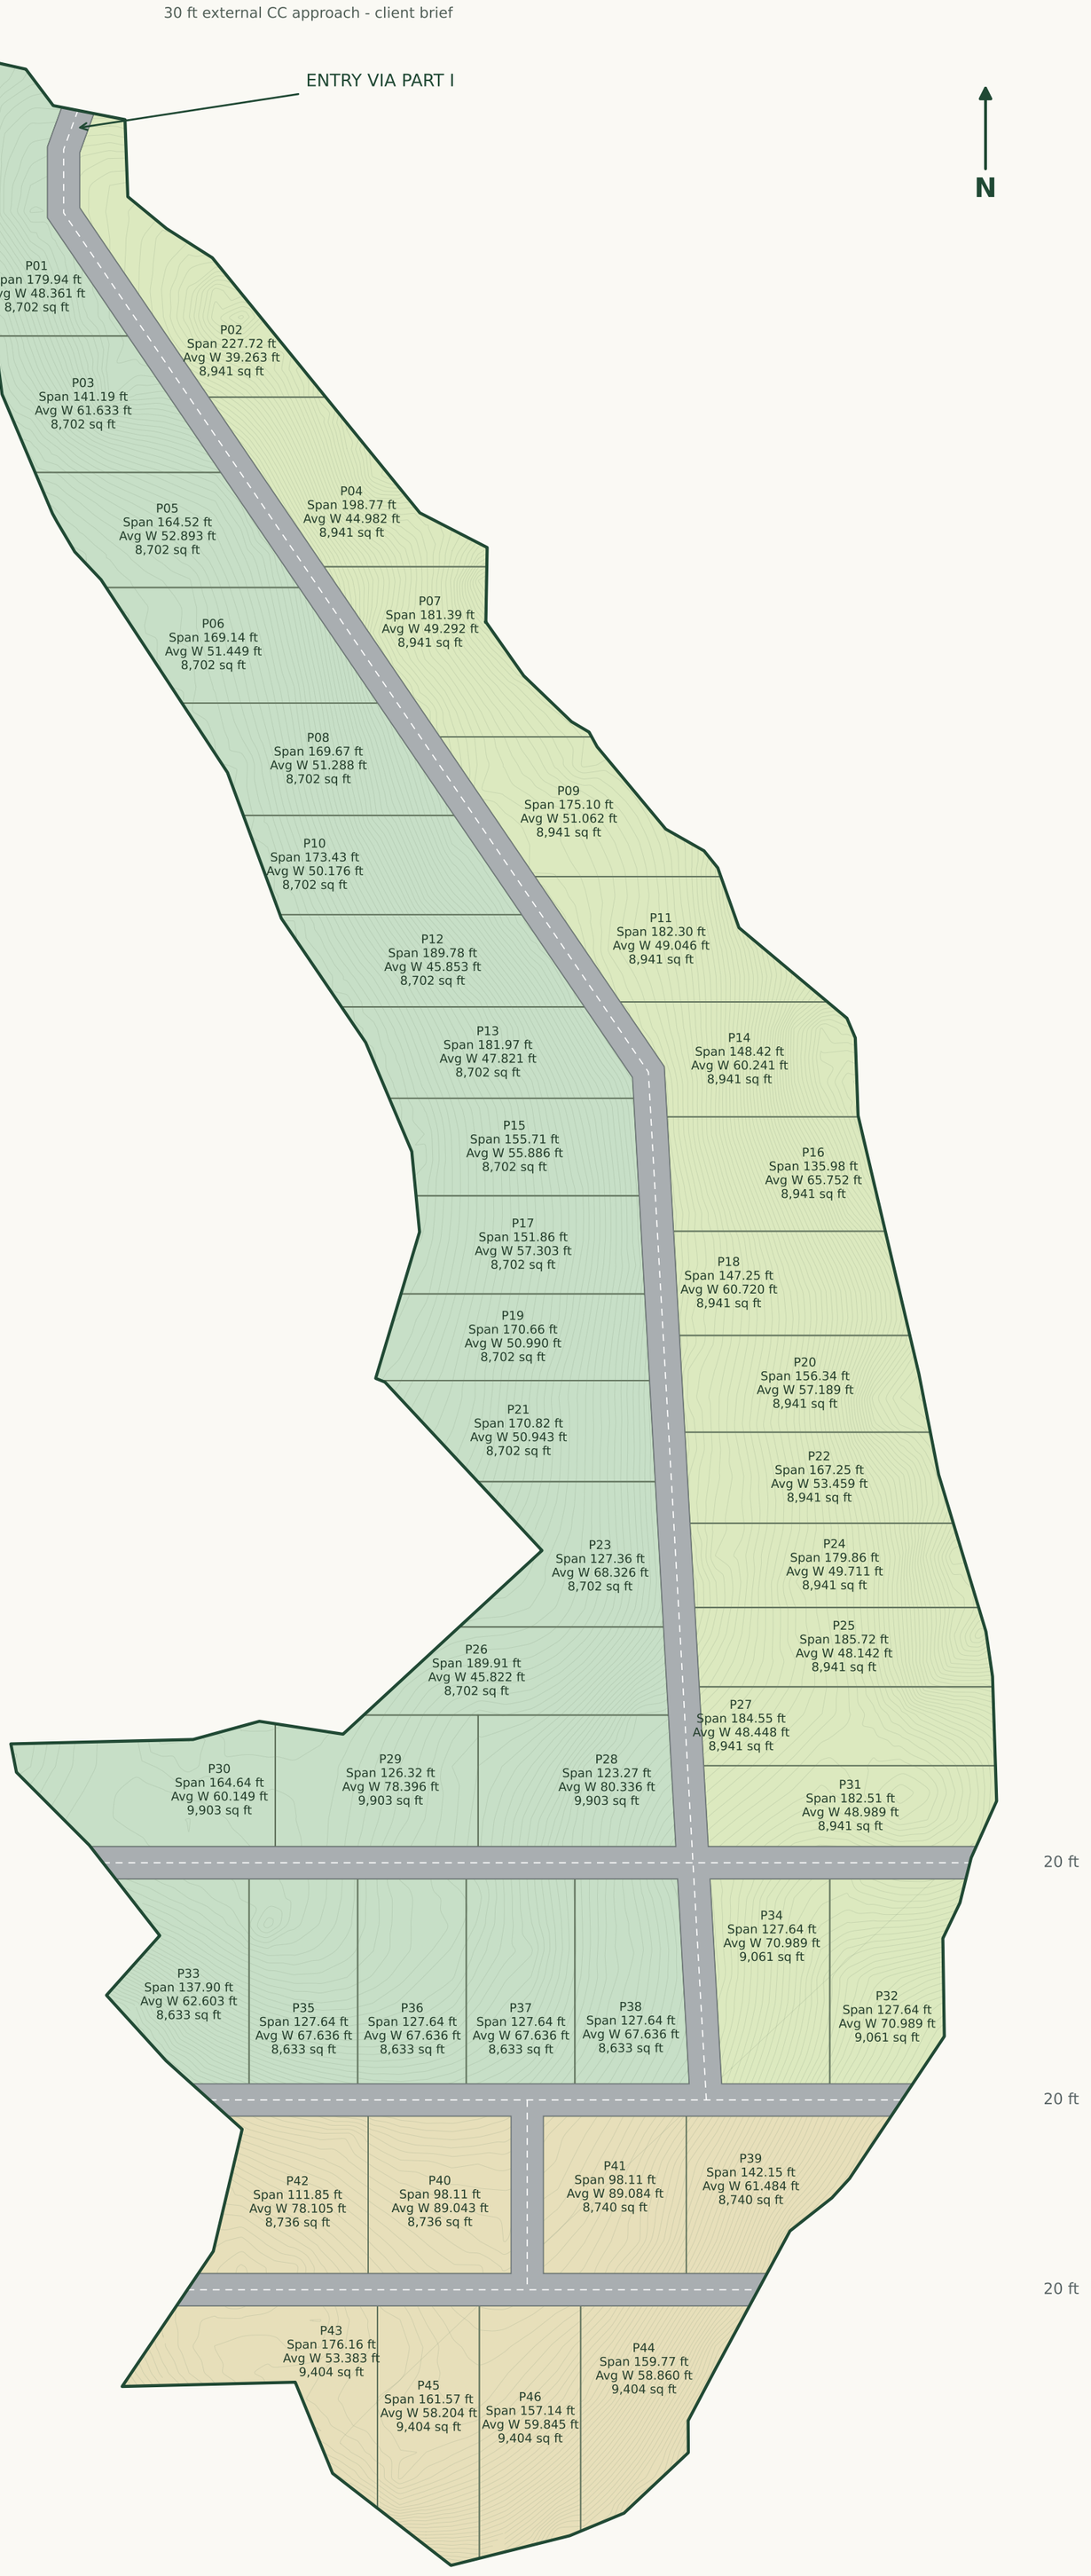

46 FARMHOUSE PLOTS

8,633-9,903 sq ft each

Labels: span and calculated average width (ft)

Span x equivalent average width = plot area

LAND ALLOCATION

Total surveyed land

465,524 sq ft

Private plots

410,564 sq ft

20 ft road corridors

54,960 sq ft

ROAD & PLOT STRUCTURE

Straight spine sections
Three cross streets + straight connector
Connected junction network
20 ft / 6.096 m road width
Every plot has road frontage
All remaining land assigned to plots

REVISION 04

Plots and internal roads only.
The previous amenity layout is replaced.
Parts I, II and III are combined.
Entry retained through Part I.

DESIGN STATUS

Proposed layout; boundary areas checked.
Road levels and cut/fill are unverified.
Irregular edge plots need building-pad and drainage checks before finalisation.

Road corridor excludes any additional width later required for services/verges.
Not a construction or approval drawing.

VERIFIED AREA-CHECK SCHEDULE

Revision 04 | P01-P23 | 46 plots in total

Plot	Length span (ft)	Eq. avg width (ft)	Area (sq ft)	Road frontage (ft)
P01	179.94	48.361	8,702	159.4
P02	227.72	39.263	8,941	202.8
P03	141.19	61.633	8,702	102.7
P04	198.77	44.982	8,941	127.7
P05	164.52	52.893	8,702	86.7
P06	169.14	51.449	8,702	86.9
P07	181.39	49.292	8,941	128.1
P08	169.67	51.288	8,702	84.7
P09	175.10	51.062	8,941	105.2
P10	173.43	50.176	8,702	74.7
P11	182.30	49.046	8,941	94.4
P12	189.78	45.853	8,702	69.6
P13	181.97	47.821	8,702	66.0
P14	148.42	60.241	8,941	80.1
P15	155.71	55.886	8,702	60.9
P16	135.98	65.752	8,941	71.3
P17	151.86	57.303	8,702	61.1
P18	147.25	60.720	8,941	65.0
P19	170.66	50.990	8,702	54.0
P20	156.34	57.189	8,941	60.3
P21	170.82	50.943	8,702	63.1
P22	167.25	53.459	8,941	56.8
P23	127.36	68.326	8,702	90.6

TOTAL PLOT AREA: 410,564 SQ FT | AVERAGE: 8,925 SQ FT

20 FT ROAD CORRIDORS: 54,960 SQ FT | UNASSIGNED LAND: 0 SQ FT

1. Length span x equivalent average width equals the displayed plot area to the nearest square foot. The width is calculated as area / span, not a measured boundary-side width. Actual side lengths appear on the plot-detail sheets. Polygon areas were independently checked from vertex coordinates.

2. 20 ft is the concept road-corridor width. Additional drains, verges or junction widening, if required during detailed design, will change the plot allocations.

3. Boundary geometry is calibrated to the survey area statement. DXF coordinates are local north-up metres, not the original cadastral coordinate frame.

4. Terrain gradients, retaining walls, cut/fill, drainage and buildable farmhouse pads remain unverified. Frontage is measured along the road corridor, not gate-opening width.

VERIFIED AREA-CHECK SCHEDULE

Revision 04 | P24-P46 | 46 plots in total

Plot	Length span (ft)	Eq. avg width (ft)	Area (sq ft)	Road frontage (ft)
P24	179.86	49.711	8,941	52.5
P25	185.72	48.142	8,941	49.5
P26	189.91	45.822	8,702	54.9
P27	184.55	48.448	8,941	49.1
P28	123.27	80.336	9,903	205.3
P29	126.32	78.396	9,903	126.3
P30	164.64	60.149	9,903	115.1
P31	182.51	48.989	8,941	217.4
P32	127.64	70.989	9,061	136.5
P33	137.90	62.603	8,633	145.0
P34	127.64	70.989	9,061	269.8
P35	127.64	67.636	8,633	135.3
P36	127.64	67.636	8,633	135.3
P37	127.64	67.636	8,633	135.3
P38	127.64	67.636	8,633	263.1
P39	142.15	61.484	8,740	203.4
P40	98.11	89.043	8,736	276.2
P41	98.11	89.084	8,740	276.3
P42	111.85	78.105	8,736	234.6
P43	176.16	53.383	9,404	165.2
P44	159.77	58.860	9,404	127.4
P45	161.57	58.204	9,404	63.5
P46	157.14	59.845	9,404	63.0

TOTAL PLOT AREA: 410,564 SQ FT | AVERAGE: 8,925 SQ FT

20 FT ROAD CORRIDORS: 54,960 SQ FT | UNASSIGNED LAND: 0 SQ FT

1. Length span x equivalent average width equals the displayed plot area to the nearest square foot. The width is calculated as area / span, not a measured boundary-side width. Actual side lengths appear on the plot-detail sheets. Polygon areas were independently checked from vertex coordinates.

2. 20 ft is the concept road-corridor width. Additional drains, verges or junction widening, if required during detailed design, will change the plot allocations.


3. Boundary geometry is calibrated to the survey area statement. DXF coordinates are local north-up metres, not the original cadastral coordinate frame.

4. Terrain gradients, retaining walls, cut/fill, drainage and buildable farmhouse pads remain unverified. Frontage is measured along the road corridor, not gate-opening width.

ACTUAL PLOT BOUNDARY MEASUREMENTS


Side lengths in feet | Measured from the concept polygon | Sketches individually scaled

P01 | 8,702 sq ft

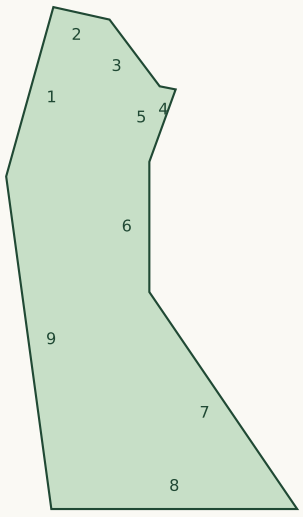


Side	Length (ft)
1	59.67
2	19.52
3	28.32
4	5.52
5	26.13
6	44.21
7	89.10
8	83.40
9	113.91

P02 | 8,941 sq ft

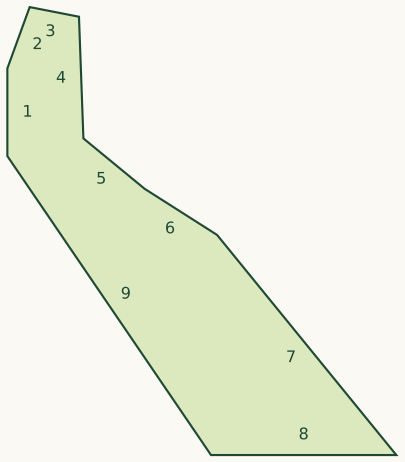


Side	Length (ft)
1	34.53
2	25.74
3	19.79
4	47.99
5	31.26
6	33.81
7	111.88
8	73.00
9	142.57

P03 | 8,702 sq ft

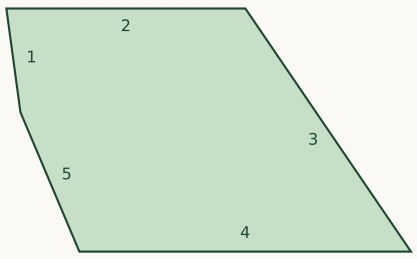


Side	Length (ft)
1	36.56
2	83.40
3	102.68
4	115.71
5	52.81

P04 | 8,941 sq ft

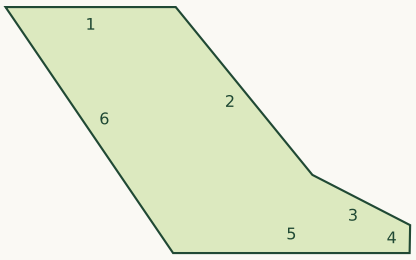


Side	Length (ft)
1	73.00
2	92.84
3	47.14
4	11.98
5	101.45
6	127.69

P05 | 8,702 sq ft



Side	Length (ft)
1	23.84
2	21.43
3	6.15
4	27.77
5	115.71
6	86.71
7	120.21
8	5.90

P06 | 8,702 sq ft




Side	Length (ft)
1	120.21
2	86.93
3	122.01
4	85.93

Side numbers refer to the sketch. Irregular-plot area uses vertex geometry, not two boundary lengths multiplied.
Coordinates are local metres in the editable DXF; verify on site before setting out.

ACTUAL PLOT BOUNDARY MEASUREMENTS


Side lengths in feet | Measured from the concept polygon | Sketches individually scaled

P07 | 8,941 sq ft

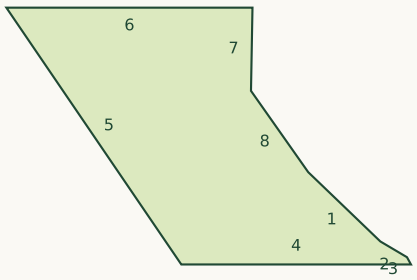


Side	Length (ft)
1	41.26
2	12.75
3	3.41
4	94.66
5	128.11
6	101.45
7	34.31
8	40.98

P08 | 8,702 sq ft




Side	Length (ft)
1	51.73
2	122.01
3	84.67
4	131.41
5	28.50

P09 | 8,941 sq ft




Side	Length (ft)
1	66.71
2	27.44
3	13.62
4	5.78
5	115.88
6	105.21
7	94.66
8	7.00

P10 | 8,702 sq ft




Side	Length (ft)
1	131.41
2	74.66
3	150.62
4	65.79

P11 | 8,941 sq ft



Side	Length (ft)
1	71.96
2	129.19
3	94.36
4	115.88
5	33.71

P12 | 8,702 sq ft



Side	Length (ft)
1	2.44
2	150.62
3	69.56
4	151.41
5	66.75


Side numbers refer to the sketch. Irregular-plot area uses vertex geometry, not two boundary lengths multiplied.
Coordinates are local metres in the editable DXF; verify on site before setting out.

ACTUAL PLOT BOUNDARY MEASUREMENTS

Side lengths in feet | Measured from the concept polygon | Sketches individually scaled


P13 | 8,702 sq ft

Side	Length (ft)
1	26.73
2	151.41
3	53.00
4	13.00
5	152.28
6	37.65




P14 | 8,941 sq ft

Side	Length (ft)
1	13.31
2	48.31
3	0.92
4	119.21
5	31.30
6	48.76
7	129.19
8	15.76




P15 | 8,702 sq ft

Side	Length (ft)
1	36.02
2	152.28
3	60.87
4	139.02
5	27.72




P16 | 8,941 sq ft

Side	Length (ft)
1	131.97
2	71.30
3	119.21
4	73.14




P17 | 8,702 sq ft

Side	Length (ft)
1	22.52
2	139.02
3	61.11
4	151.86
5	40.29



P18 | 8,941 sq ft

Side	Length (ft)
1	143.59
2	64.99
3	131.97
4	66.67




Side numbers refer to the sketch. Irregular-plot area uses vertex geometry, not two boundary lengths multiplied.
Coordinates are local metres in the editable DXF; verify on site before setting out.

ACTUAL PLOT BOUNDARY MEASUREMENTS

Side lengths in feet | Measured from the concept polygon | Sketches individually scaled


P19 | 8,702 sq ft

Side	Length (ft)
1	54.85
2	151.86
3	54.00
4	167.26
5	3.66




P20 | 8,941 sq ft

Side	Length (ft)
1	36.92
2	152.94
3	60.28
4	143.59
5	24.61




P21 | 8,702 sq ft

Side	Length (ft)
1	2.57
2	167.26
3	63.07
4	110.58
5	84.80




P22 | 8,941 sq ft

Side	Length (ft)
1	31.64
2	164.05
3	56.77
4	152.94
5	26.88




P23 | 8,702 sq ft

Side	Length (ft)
1	110.58
2	90.57
3	127.36
4	70.22
5	58.55

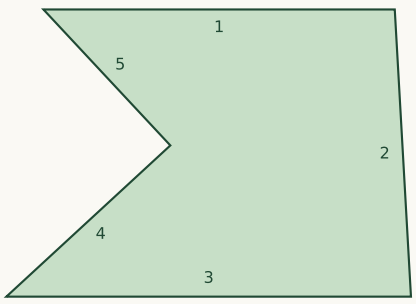

P24 | 8,941 sq ft

Side	Length (ft)
1	176.90
2	52.53
3	164.05
4	54.78




Side numbers refer to the sketch. Irregular-plot area uses vertex geometry, not two boundary lengths multiplied.
Coordinates are local metres in the editable DXF; verify on site before setting out.

ACTUAL PLOT BOUNDARY MEASUREMENTS

Side lengths in feet | Measured from the concept polygon | Sketches individually scaled


P25 | 8,941 sq ft

Side	Length (ft)
1	28.25
2	6.48
3	182.94
4	49.46
5	176.90
6	15.61



P26 | 8,702 sq ft

Side	Length (ft)
1	189.91
2	80.90
3	127.36
4	54.94




P27 | 8,941 sq ft

Side	Length (ft)
1	181.78
2	49.10
3	182.94
4	49.05




P28 | 9,903 sq ft

Side	Length (ft)
1	81.99
2	123.27
3	81.86
4	118.66

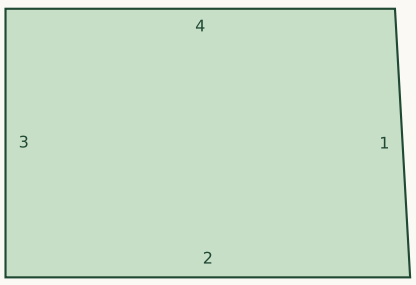


P29 | 9,903 sq ft

Side	Length (ft)
1	17.44
2	71.26
3	81.86
4	126.32
5	76.52
6	42.74

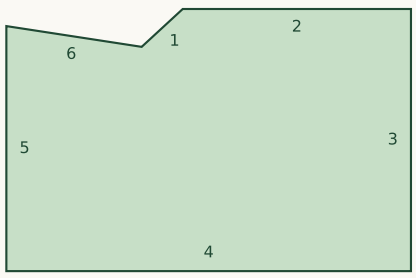

P30 | 9,903 sq ft

Side	Length (ft)
1	113.55
2	42.78
3	9.99
4	76.52
5	115.06
6	1.24
7	64.12
8	18.00




Side numbers refer to the sketch. Irregular-plot area uses vertex geometry, not two boundary lengths multiplied.
Coordinates are local metres in the editable DXF; verify on site before setting out.

ACTUAL PLOT BOUNDARY MEASUREMENTS


Side lengths in feet | Measured from the concept polygon | Sketches individually scaled

P31 | 8,941 sq ft




Side	Length (ft)
1	31.15
2	166.92
3	50.50
4	181.78
5	22.01

P32 | 9,061 sq ft

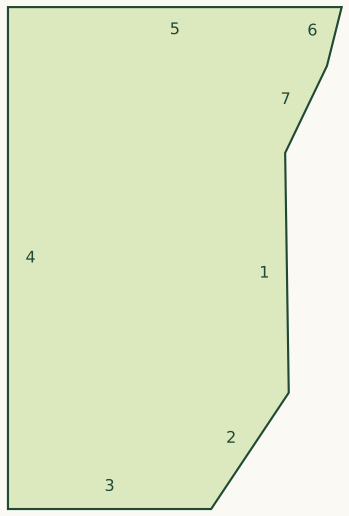


Side	Length (ft)
1	60.98
2	35.55
3	51.65
4	127.64
5	84.83
6	15.40
7	24.57

P33 | 8,633 sq ft

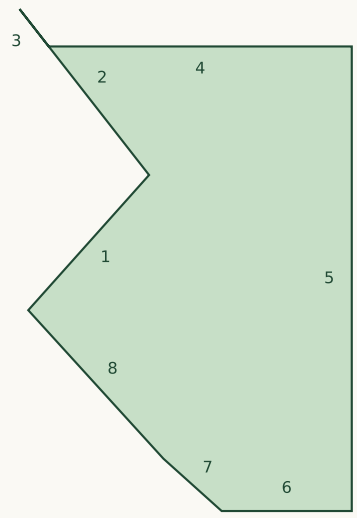


Side	Length (ft)
1	49.80
2	57.82
3	13.02
4	83.23
5	127.64
6	35.73
7	21.50
8	55.16

P34 | 9,061 sq ft

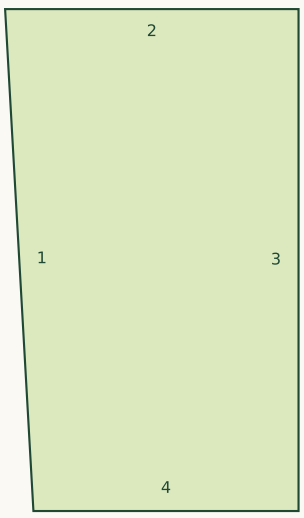


Side	Length (ft)
1	127.84
2	74.59
3	127.64
4	67.39

P35 | 8,633 sq ft

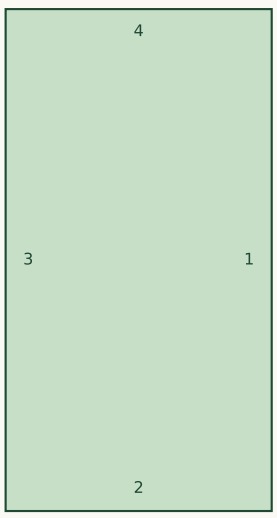

Side	Length (ft)
1	127.64
2	67.64
3	127.64
4	67.64

P36 | 8,633 sq ft

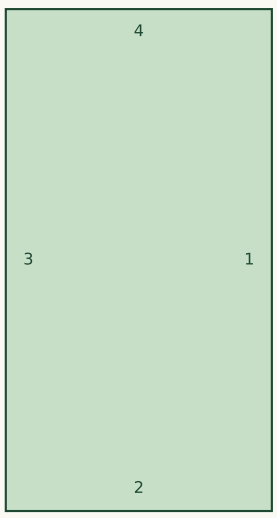


Side	Length (ft)
1	127.64
2	67.64
3	127.64
4	67.64

Side numbers refer to the sketch. Irregular-plot area uses vertex geometry, not two boundary lengths multiplied.
Coordinates are local metres in the editable DXF; verify on site before setting out.

ACTUAL PLOT BOUNDARY MEASUREMENTS


Side lengths in feet | Measured from the concept polygon | Sketches individually scaled

P37 | 8,633 sq ft

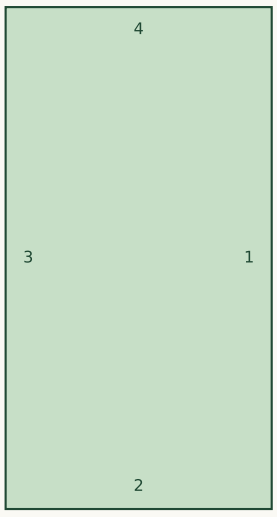


Side	Length (ft)
1	127.64
2	67.64
3	127.64
4	67.64

P38 | 8,633 sq ft

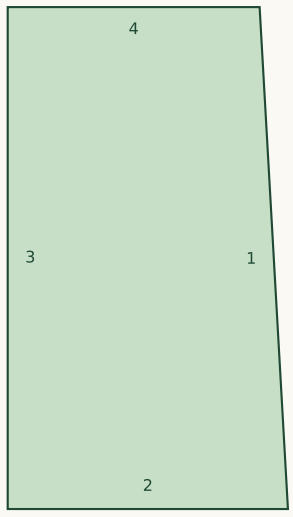


Side	Length (ft)
1	127.84
2	71.24
3	127.64
4	64.04

P39 | 8,740 sq ft

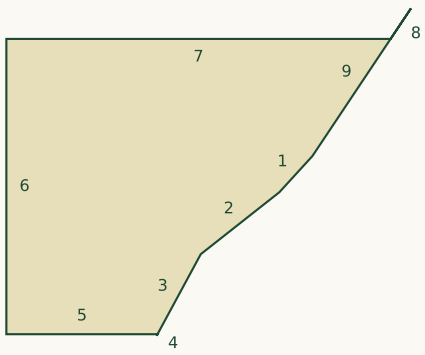


Side	Length (ft)
1	16.28
2	33.25
3	30.80
4	0.58
5	50.19
6	98.11
7	127.61
8	12.20
9	58.97

P40 | 8,736 sq ft

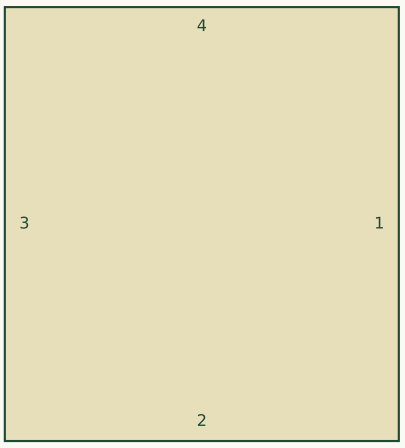


Side	Length (ft)
1	98.11
2	89.05
3	98.11
4	89.05

P41 | 8,740 sq ft

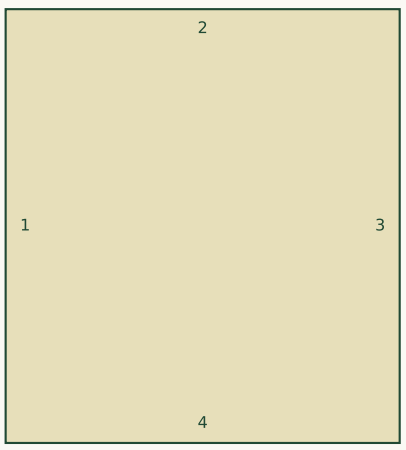

Side	Length (ft)
1	98.11
2	89.09
3	98.11
4	89.09

P42 | 8,736 sq ft

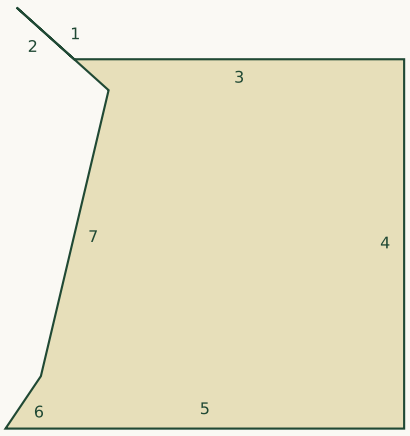


Side	Length (ft)
1	32.85
2	20.55
3	87.62
4	98.11
5	105.86
6	16.80
7	78.06

Side numbers refer to the sketch. Irregular-plot area uses vertex geometry, not two boundary lengths multiplied.
Coordinates are local metres in the editable DXF; verify on site before setting out.

ACTUAL PLOT BOUNDARY MEASUREMENTS


Side lengths in feet | Measured from the concept polygon | Sketches individually scaled

P43 | 9,404 sq ft

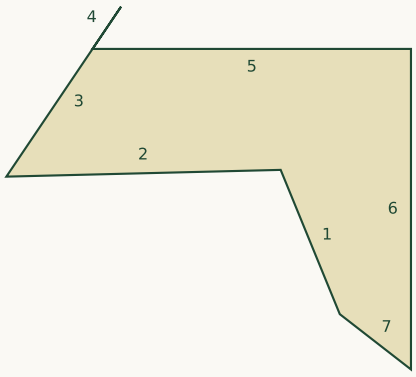


Side	Length (ft)
1	61.30
2	107.84
3	80.60
4	20.03
5	125.15
6	126.01
7	35.42

P44 | 9,404 sq ft

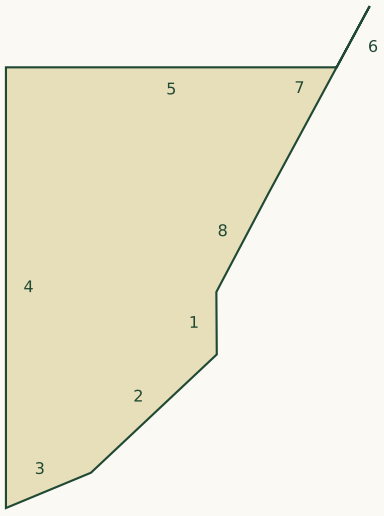


Side	Length (ft)
1	19.89
2	54.96
3	29.29
4	140.28
5	105.21
6	22.16
7	67.42
8	35.83

P45 | 9,404 sq ft



Side	Length (ft)
1	57.96
2	126.01
3	63.49
4	157.14
5	18.26

P46 | 9,404 sq ft



Side	Length (ft)
1	57.99
2	157.14
3	63.03
4	140.28
5	7.33

Side numbers refer to the sketch. Irregular-plot area uses vertex geometry, not two boundary lengths multiplied.
Coordinates are local metres in the editable DXF; verify on site before setting out.
